FLASHING ORDER

FO-001001 · export 2

FROM
Blue Leaf Building (sandbox)
Sandbox address

SUPPLIER
Fielders (SANDBOX — not a real contact)
Attn: Sandbox orders
00 0000 0000
orders@example.invalid


JOB
Sandbox job — your drawings (Takeoff test)
Deliver to:
1 Example Street, Testville (synthetic)
Required: 2026-10-27
Site contact: Site lead 0400 000 000

Notes: Example order — synthetic data

All dimensions in mm. Lengths are FINISHED order lengths. Girth is indicative only (no bend deduction) — supplier fabrication instructions take precedence.

P1 — Apron flashing

COLORBOND · Monument · 0.55 BMT · Flashing

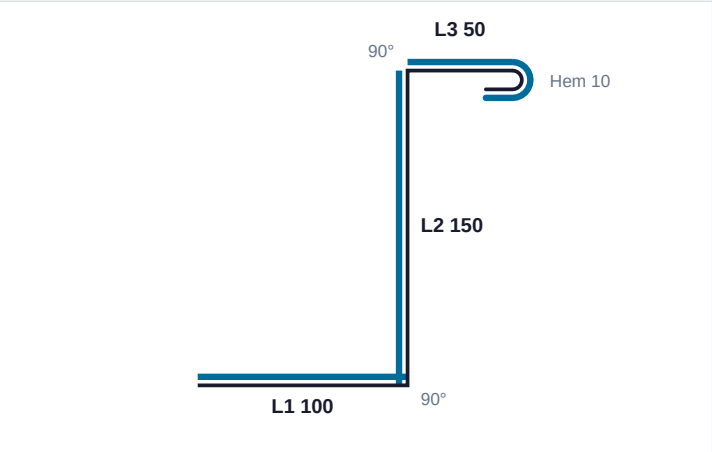

Coated face (left side travelling L1 -> L3)

DIMENSIONS
L1 100 mm
L2 150 mm
L3 50 mm
B1 90° fold left
B2 90° fold right
Start: plain
End: closed hem 10 mm (right)
Indicative girth 310 mm

QTY	FINISHED LENGTH (mm)	LM	HANDLING
1 ×	6,100	6.100	Long piece — handle with care
2 ×	4,600	9.200	-
1 ×	3,200	3.200	-


4 pieces · 18.500 LM

FLASHING ORDER

FO-001001 · export 2 (continued)

P2 — Barge flashing

COLORBOND · Surfmist · 0.55 BMT · Flashing

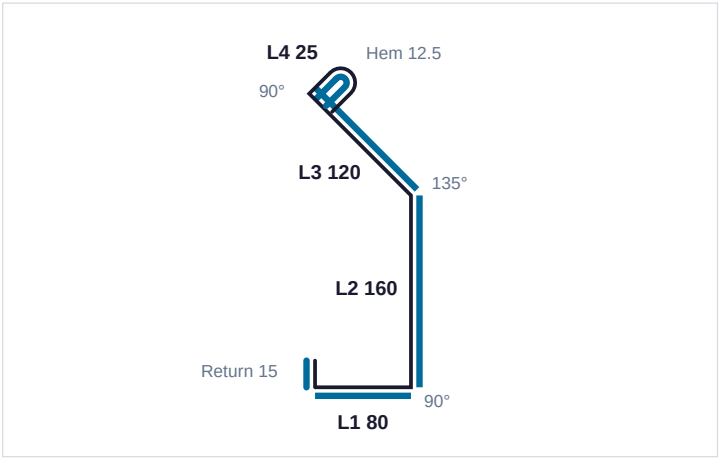

Coated face (right side travelling L1 -> L4)

DIMENSIONS


L1 80 mm
L2 160 mm
L3 120 mm
L4 25 mm
B1 90° fold left
B2 135° fold left
B3 90° fold right
Start: open return 15 mm (left)
End: closed hem 12.5 mm (right)
Indicative girth 412.5 mm

QTY	FINISHED LENGTH (mm)	LM	HANDLING
2 ×	4,600	9.200	-
2 ×	3,700	7.400	-
4 ×	2,400	9.600	-

8 pieces · 26.200 LM

P3 — Std valley gutter (example)

COLORBOND · Basalt · 0.55 BMT · Flashing

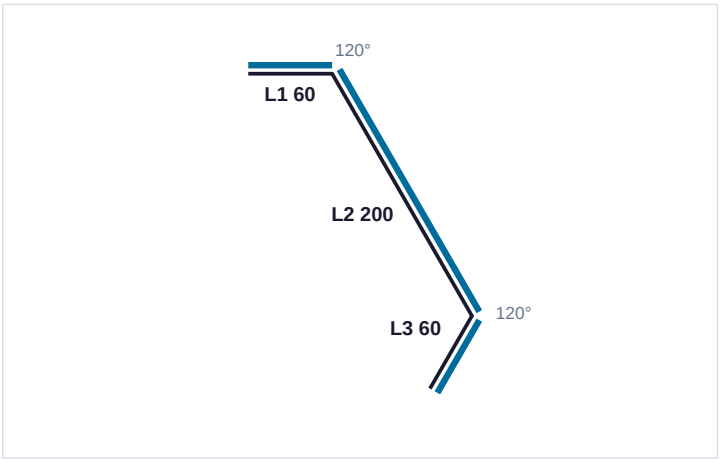

Coated face (left side travelling L1 -> L3)

DIMENSIONS

L1 60 mm
L2 200 mm
L3 60 mm
B1 120° fold right
B2 120° fold right
Start: plain
End: plain
Indicative girth 320 mm

QTY	FINISHED LENGTH (mm)	LM	HANDLING
1 ×	4,400	4.400	-

1 piece · 4.400 LM

Order total: 13 pieces · 49.100 LM · 1 long piece flagged

This document lists quantities and profiles only. It is not a price or a contract. Confirm product availability, colour and fabrication allowances with the supplier.
