DRAFT FLASHING ORDER

FO-001001 · export 1

FROM
Blue Leaf Building
ABN 00 000 000 000
Sample office address
08 1111 1111
office@example.test

SUPPLIER
Fielders (sample branch)
Attn: Orders desk
08 0000 0000
orders@example.test

JOB
1 Sample Street (Sample client)
Deliver to:
1 Sample Street, Testville
Required: 2026-10-20
Site contact: Lee 0400 000 000


Notes: Sample — synthetic data

All dimensions in mm. Lengths are FINISHED order lengths. Girth is indicative only (no bend deduction) — supplier fabrication instructions take precedence.

P1 — Apron (solid)

COLORBOND · Monument · 0.55 BMT · solid

Confirm availability with supplier

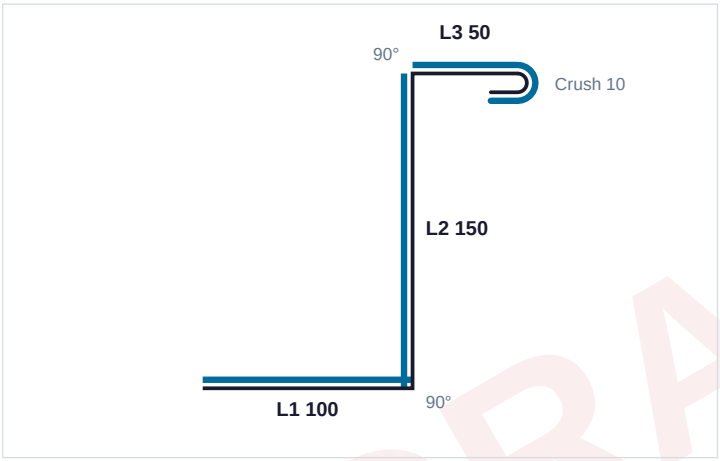

Painted (colour) face — left side travelling L1 -> L3

DIMENSIONS
L1 100 mm
L2 150 mm
L3 50 mm
B1 90° fold left
B2 90° fold right
Start: plain
End: crush fold (closed hem) 10 mm, folds right
Indicative girth 310 mm

QTY	FINISHED LENGTH (mm)	LM	HANDLING
1 ×	4,600	4.600	-

1 piece · 4.600 LM

DRAFT


DRAFT FLASHING ORDER

FO-001001 · export 1 (continued)

P2 — Apron (zinc)

ZINCALUME · natural (unpainted) · 0.5 BMT · solid

Confirm availability with supplier

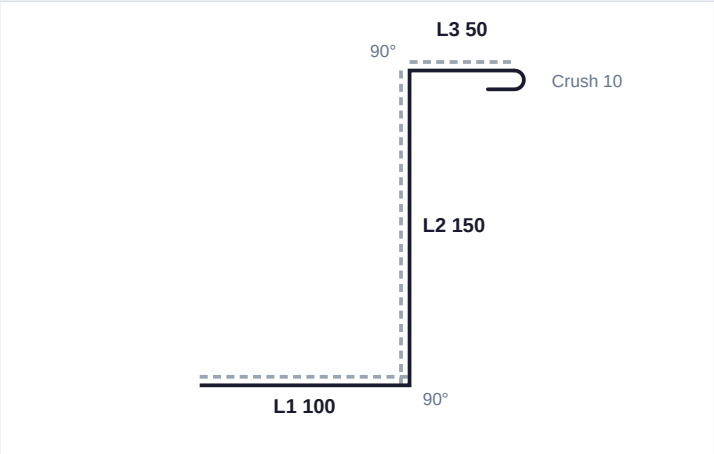

Reference side (unpainted — no colour face) — left side travelling L1 -> L3

DIMENSIONS

L1 100 mm
L2 150 mm
L3 50 mm
B1 90° fold left
B2 90° fold right
Start: plain
End: crush fold (closed hem) 10 mm, folds right
Indicative girth 310 mm

QTY	FINISHED LENGTH (mm)	LM	HANDLING
1 ×	4,600	4.600	-


1 piece · 4.600 LM

P3 — Vent flashing

COLORBOND · Surfmist · 0.55 BMT

PERFORATED · round holes 3 mm @ 6 mm pitch · 11% open · legs L2 · solid margin 10 mm

Confirm availability with supplier

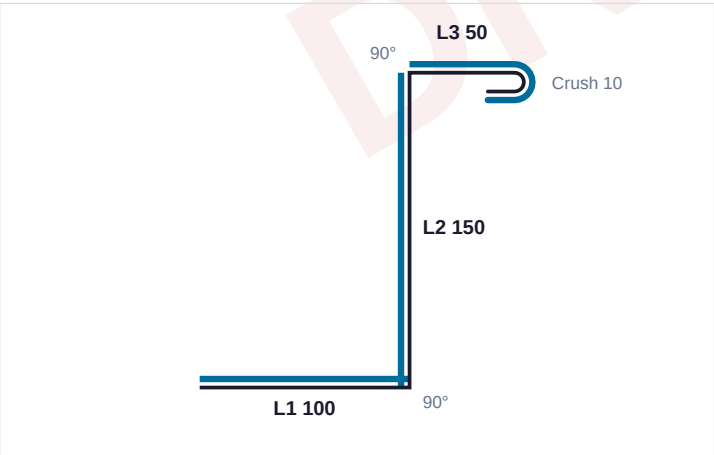

Painted (colour) face — left side travelling L1 -> L3

DIMENSIONS

L1 100 mm
L2 150 mm
L3 50 mm
B1 90° fold left
B2 90° fold right
Start: plain
End: crush fold (closed hem) 10 mm, folds right
Indicative girth 310 mm

QTY	FINISHED LENGTH (mm)	LM	HANDLING
1 ×	4,600	4.600	-

1 piece · 4.600 LM

Order total: 3 pieces · 13.800 LM

This document lists quantities and profiles only. It is not a price or a contract. Confirm product availability, colour and fabrication allowances with the supplier.

DRAFT
